


Tisbury School Renovation/Addition

Project Update Newsletter

February 2023

The Tisbury School Project remains on schedule and within budget. Installation of the site infrastructure drainage is underway in the east field. And at the west corner of the building, installation of Secant Piles continues and will be completed in a few weeks. Subsequently, Soldier Piles and Lagging will be placed to allow the excavation to begin for the foundation walls for the new building addition. All abatement tasks for the interior of the existing school have been completed; except for the window caulking abatement, which will take place once windows are removed. Demolition on the third floor is complete. Second-floor demolition is currently at 50%. And once the second-floor demolition is complete, the crew will move to the first floor for approximately four more weeks to complete the demolition phase of the project.

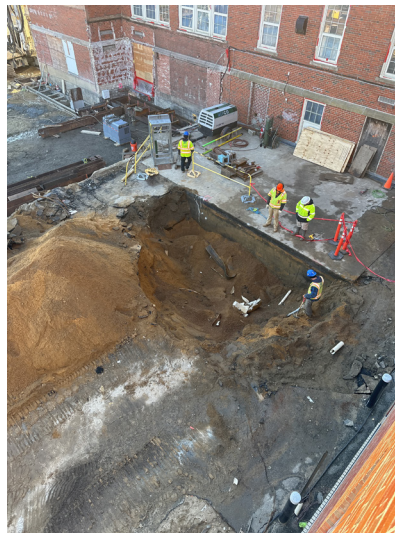

Contact Us!

School Building Committee:
www.tisbury-school-project.com
tisburyschoolproject@gmail.com

Owner's Project Manager:
Michael Owen (401) 640-1641
Aditya Modi (617) 516-4953

1/23/2023 – 2/10/2023

External Testing and Inspections team to begin required inspections for rebar, concrete, soils, and subgrade



2/13/2023 – 2/24/2023

Interior demolition for all three floors



2/27/2023 – 3/3/2023

Drilling of soldier piles and lagging for stabilization of earth prior to excavation operations *



**sound generating activity*

We Are Here

2/13/2023 – 2/24/2023

Secant pile systems drilling and installation *



**sound generating activity*

2/21/2023 – 3/3/2023

Third floor structural remediation, blocking, and joist structure enhancements



2/27/2023 – 3/3/2023

Sitework - Excavation for building foundations for new addition

